

經濟部水利署第九河川分署

秀姑巒溪流域整體改善調適大平台會議

羅山遊憩區觀光發展規劃執行情形


交通部觀光署花東縱谷國家風景區管理處

主講人：洪副處長肇昌

113年10月28日

計畫範圍與目標

以羅山遊客中心為核心，配合遊客服務，打造成為提供縱谷中區旅遊資訊的主要遊客中心外，並串聯遊憩區範圍內之羅山有機村、富里鄉幸福廣場、羅山富里鄉農會，羅山瀑布步道、大魚池泥火山、九岸溪西畔、羅山之丘等

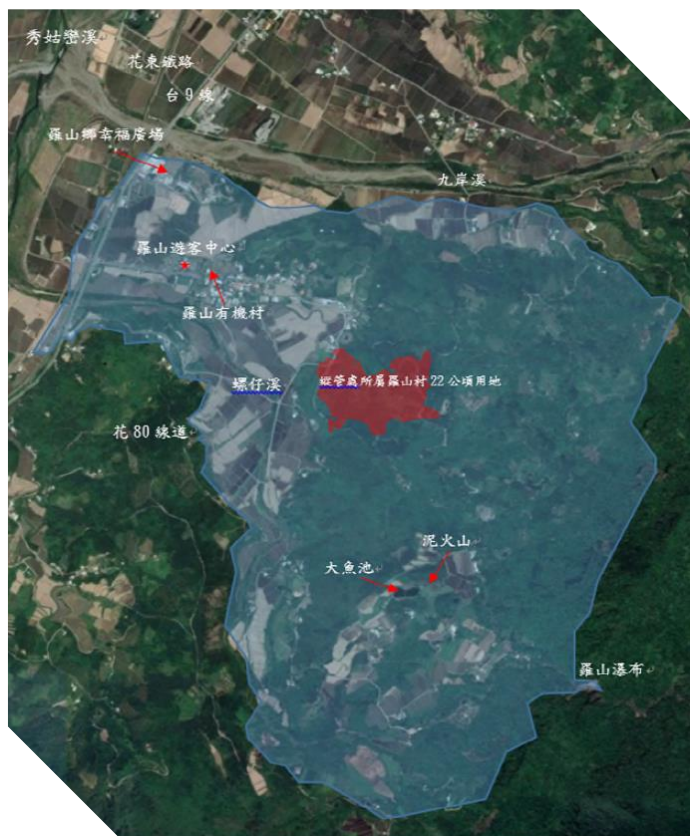

羅山遊客中心至幸福廣場自行車道改善工程

- 建設總經費：700萬元
- 竣工日期：112年12月8日
- 融入地方特色、減量設計以維護鄉村景觀，建立結合**體驗旅遊**與**生活美學**的**休閒景觀路廊**，後續由花蓮縣富里鄉公所管理維護

改善範圍



拓寬模擬圖



改善完成1




改善完成2



羅山之丘景觀生態步道改善工程

- 建設總經費1,700萬元
- 開工日期：113年6月3日
- 預定完工日期：113年11月18日(進度87%)
- 以不破壞既有環境工法，新建聯絡生態步道及自然生態步道，結合區內自然環境建置更新導覽系統，使遊客能夠親近大自然並瞭解羅山故事內容的深度旅遊

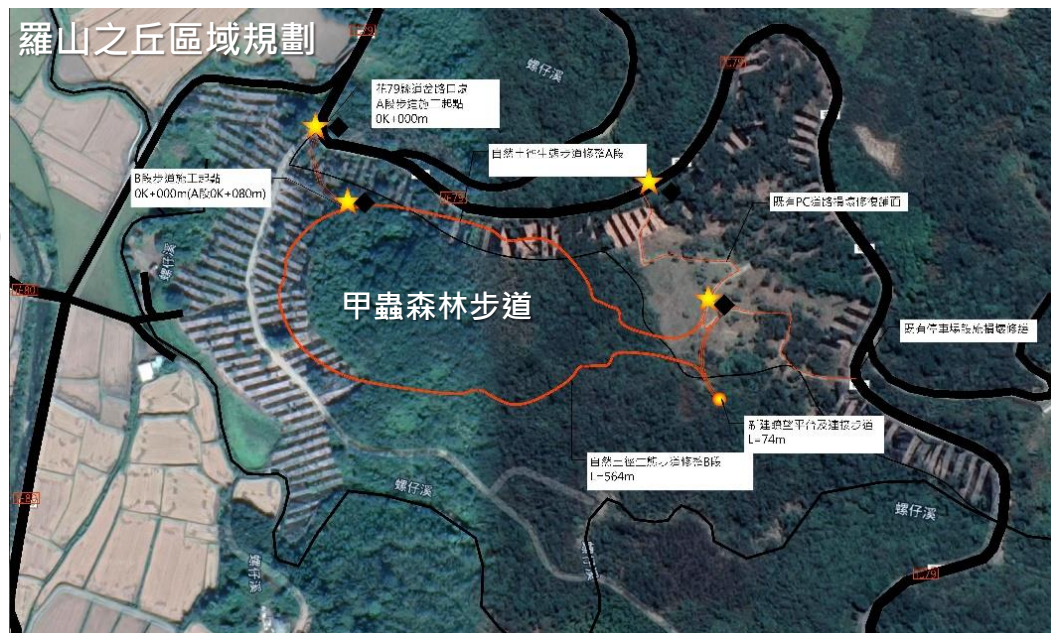


▽ 仿枕木階梯示意圖

△ 新建聯絡生態步道示意圖



△ 新建生態步道示意圖

▽ 羅山遊憩區新建平台模擬圖

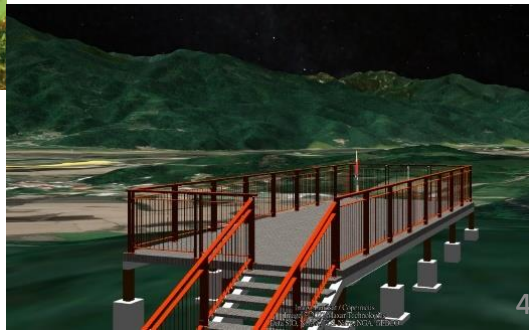

羅山遊客中心周邊遊憩設施營造工程

- 建設總經費2,000萬元
- 開工日期：113年5月13日
- 預定完工日期：113年11月22日(進度72%)
- 配合縱谷原遊會主題及活動需求，規劃增設舞台、眺景、休憩等設施，並結合羅山遊客中心之遊憩服務機能，創造周邊開放空間亮點，呼應相對應之活動空間，提昇遊憩服務品質



羅山遊客中心周邊改善模擬圖1



螺山憶稻模擬圖



原舞台模擬圖



羅山遊客中心周邊改善模擬圖2

An aerial photograph of a park featuring a large, multi-story building with a traditional Chinese-style roof. The park is filled with lush green trees and has a complex system of winding, paved paths. In the background, there are rolling hills and mountains under a blue sky with some clouds. A semi-circular road with a central green island is visible on the right side of the image.

感謝聆聽
敬請指教

縱覽島源山川，谷豐瑰寶逸趣
原味花東
